DEMONSTRATION ONLY — NOT A QUALIFIED PROCEDURE; THE FACILITY OWNER'S QUALIFIED PROCEDURES AND APPLICABLE CODES GOVERN.

WO-200-04 — Ultrasonic thickness survey of 6"-P300-P-1011

Area	A200 Vessels and column	**Task**	UT Ultrasonic thickness survey
Priority	2 (integrity)	**Issued by**	Facility owner (demonstration)
Primary asset	C-101 — C-101 vertical vessel 48" ID × 240" T/T — E 68'-6" N 25'-0" EL 100'-8-1/4"		
Equipment	C-101	**Lines**	6"-P300-P-1011
Isometrics	ISO-P-1011 (owner's drawings, attached)		
Permits	General work permit		

Reason

Thickness survey of the column overhead line.

Scope of work

1. Erect access and remove insulation at the TMLs where fitted (class H300).
2. Calibrate the thickness gauge on a step block covering 0.21875 in.
3. Take four readings 90° apart at each of the 15 TMLs (SW-WO-6).
4. Report readings against the owner's minimum wall; raise a spool replacement for any reading below it.

Affected items: 6"-P300-P-1011/el8, 6"-P300-P-1011/p9, 6"-P300-P-1011/el10, 6"-P300-P-1011/p11, 6"-P300-P-1011/el12, 6"-P300-P-1011/p13, 6"-P300-P-1011/T:3/4"-P300-I-7011, 6"-P300-P-1011/el16, 6"-P300-P-1011/el18, 6"-P300-P-1011/p19, 6"-P300-P-1011/el20, 6"-P300-P-1011/p21, 6"-P300-P-1011/el22, 6"-P300-P-1011/p23, 6"-P300-P-1011/el24

Rules: SW-ITP-1, SW-ITP-2, SW-ITP-3, SW-WO-1, SW-WO-2, SW-WO-6, SW-WO-7

Owner's isometric drawings (SW-IMP-6)

Drawing	Line drawn	Work line	Sheets	Match to the plant model
ISO-P-1011	6"-P300-P-1011	6"-P300-P-1011	2	agrees with the model

ISO-P-1011 (PDF): ../isometrics-imported/ISO-P-1011.pdf — the sheets that hold the work follow the ITP.

Assets in the plant model (SW-WO-7)

Tag	Kind	Description	Line	Location
C-101	equipment	C-101 vertical vessel 48" ID × 240" T/T		E 68'-6" N 25'-0" EL 100'-8-1/4"
6"-P300-P-1011/el8	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 68'-6" N 24'-7" EL 129'-7"
6"-P300-P-1011/p9	item	PIPE 6" P300 BEVELLED ENDS	6"-P300-P-1011	E 68'-6" N 17'-9" EL 130'-0"
6"-P300-P-1011/el10	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 68'-6" N 10'-11" EL 129'-7"
6"-P300-P-1011/p11	item	PIPE 6" P300 BEVELLED ENDS	6"-P300-P-1011	E 68'-6" N 10'-6" EL 124'-6"
6"-P300-P-1011/el12	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 68'-6" N 10'-1" EL 119'-5"
6"-P300-P-1011/p13	item	PIPE 6" P300 BEVELLED ENDS	6"-P300-P-1011	E 68'-6" N 5'-3-1/2" EL 119'-0"
6"-P300-P-1011/T:3/4"-P300-I-7011	item	TEE REDUCING 6" × 3/4" P300	6"-P300-P-1011	E 68'-6" N 6" EL 119'-0"
6"-P300-P-1011/el16	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 68'-6" N -7" EL 118'-7"
6"-P300-P-1011/el18	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 68'-11" N -12" EL 117'-5"
6"-P300-P-1011/p19	item	PIPE 6" P300 BEVELLED ENDS	6"-P300-P-1011	E 78'-9" N -12" EL 117'-0"
6"-P300-P-1011/el20	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 88'-7" N -12" EL 116'-7"
6"-P300-P-1011/p21	item	PIPE 6" P300 BEVELLED ENDS	6"-P300-P-1011	E 89'-0" N -12" EL 114'-9"
6"-P300-P-1011/el22	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 89'-0" N -7" EL 112'-11"
6"-P300-P-1011/p23	item	PIPE 6" P300 BEVELLED ENDS	6"-P300-P-1011	E 89'-0" N 12'-0" EL 112'-6"
6"-P300-P-1011/el24	item	ELBOW 90° R = 5/3 OD 6" P300	6"-P300-P-1011	E 89'-0" N 24'-7" EL 112'-1"

Inspections

Id	Inspection	Criteria	Basis
WO-200-04-I1	Ultrasonic thickness at 15 TMLs, four readings each	Nominal wall 0.21875 in; each reading above the owner's minimum wall	SW-WO-6

Thickness monitoring locations (SW-WO-6)

TML	Item	Location	Position	Nominal wall	R1	R2	R3	R4
WO-200-04-TML01	6"-P300-P-1011/el8	Elbow 6"-P300-P-1011/el8 extrados	E 68'-6" N 24'-11-3/16" EL 129'-11-3/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML02	6"-P300-P-1011/p9	Pipe 6"-P300-P-1011/p9 mid-length	E 68'-6" N 17'-9" EL 130'-0"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML03	6"-P300-P-1011/el10	Elbow 6"-P300-P-1011/el10 extrados	E 68'-6" N 10'-6-13/16" EL 129'-11-3/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML04	6"-P300-P-1011/p11	Pipe 6"-P300-P-1011/p11 mid-length	E 68'-6" N 10'-6" EL 124'-6"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML05	6"-P300-P-1011/el12	Elbow 6"-P300-P-1011/el12 extrados	E 68'-6" N 10'-5-3/16" EL 119'-13/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML06	6"-P300-P-1011/p13	Pipe 6"-P300-P-1011/p13 mid-length	E 68'-6" N 5'-3-1/2" EL 119'-0"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML07	6"-P300-P-1011/T:3/4"-P300-I-7011	Tee 6"-P300-P-1011/T:3/4"-P300-I-7011 branch outlet	E 68'-6" N 6" EL 119'-0"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML08	6"-P300-P-1011/el16	Elbow 6"-P300-P-1011/el16 extrados	E 68'-6" N -11-3/16" EL 118'-11-3/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML09	6"-P300-P-1011/el18	Elbow 6"-P300-P-1011/el18 extrados	E 68'-6-13/16" N -12" EL 117'-13/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML10	6"-P300-P-1011/p19	Pipe 6"-P300-P-1011/p19 mid-length	E 78'-9" N -12" EL 117'-0"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML11	6"-P300-P-1011/el20	Elbow 6"-P300-P-1011/el20 extrados	E 88'-11-3/16" N -12" EL 116'-11-3/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML12	6"-P300-P-1011/p21	Pipe 6"-P300-P-1011/p21 mid-length	E 89'-0" N -12" EL 114'-9"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML13	6"-P300-P-1011/el22	Elbow 6"-P300-P-1011/el22 extrados	E 89'-0" N -11-3/16" EL 112'-6-13/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML14	6"-P300-P-1011/p23	Pipe 6"-P300-P-1011/p23 mid-length	E 89'-0" N 12'-0" EL 112'-6"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____
WO-200-04-TML15	6"-P300-P-1011/el24	Elbow 6"-P300-P-1011/el24 extrados	E 89'-0" N 24'-11-3/16" EL 112'-5-3/16"	0.21875 in	0°: ____	90°: ____	180°: ____	270°: ____

Inspection and test plan (SW-ITP-1..3)


H hold · W witness · R review · S surveillance. Status: accepted / rejected / not applicable.

#	Activity	Reference	Acceptance	Record	Contr.	Owner	3rd party	Status	Signed (contr. / owner / 3rd)	Date	Remark
1	Gauge calibrated on a step block; operator qualification checked	Owner UT procedure	Calibration within the owner's tolerance	Calibration record	R	R	R				
2	Readings at 15 TMLs	SW-WO-6	Four readings per TML recorded	Thickness record per TML	S	S	S				
3	Results reviewed against the owner's minimum wall	Owner integrity procedure	Every reading above the minimum, or a work order raised	Signed thickness report	R	H	R				
4	Insulation and access reinstated; work order handed back	SW-ITP-3	All activities accepted	Signed ITP	H	H	R				

Where the work is on the owner's drawings (SW-IMP-8)

Each affected item, replaced weld and isolation point, with the drawing and sheet that hold it and the weld label printed there. The sheets follow, copied unchanged.

Tag	Role	Drawing	Sheet	Weld label
6"-P300-P-1011/el8	affected	ISO-P-1011	1	
6"-P300-P-1011/p9	affected	ISO-P-1011	1	
6"-P300-P-1011/el10	affected	ISO-P-1011	1	
6"-P300-P-1011/p11	affected	ISO-P-1011	1	
6"-P300-P-1011/el12	affected	ISO-P-1011	1	
6"-P300-P-1011/p13	affected	ISO-P-1011	1	
6"-P300-P-1011/T:3/4"-P300-I-7011	affected	ISO-P-1011	1	
6"-P300-P-1011/el16	affected	ISO-P-1011	1	
6"-P300-P-1011/el18	affected	ISO-P-1011	1	
6"-P300-P-1011/p19	affected	ISO-P-1011	2	
6"-P300-P-1011/el20	affected	ISO-P-1011	2	
6"-P300-P-1011/p21	affected	ISO-P-1011	2	
6"-P300-P-1011/el22	affected	ISO-P-1011	2	
6"-P300-P-1011/p23	affected	ISO-P-1011	2	
6"-P300-P-1011/el24	affected	ISO-P-1011	2	

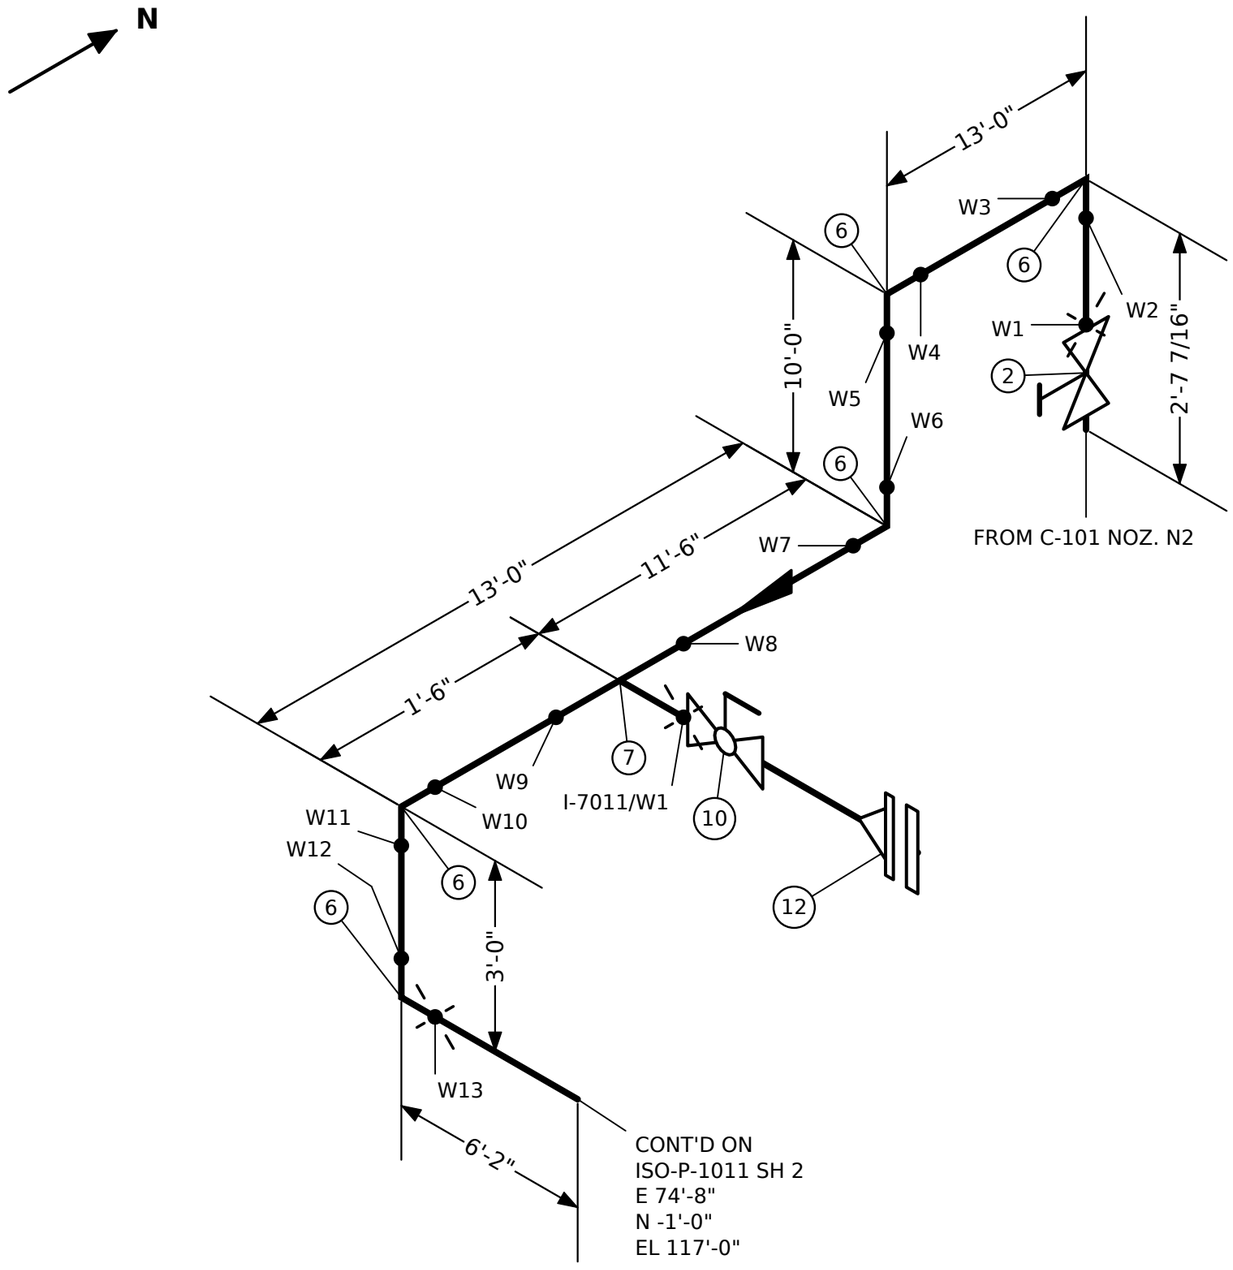

BILL OF MATERIALS

PT	QTY	NPS	DESCRIPTION
1	2	6"	GASKET 6" P300 COMPRESSED SHEET
2	1	6"	VALVE, GATE, WEDGE, OS&Y 6" P300
3	2	6"	STUD SET 8 × 0.625" × 4" WITH 2 NUTS, FOR 6" P300
4	1	6"	FLANGE WELD-NECK 6" P300 RAISED FACE
5	37'-1 1/4"	6"	PIPE 6" P300 BEVELLED ENDS
6	5	6"	ELBOW 90° R = 5/3 OD 6" P300
7	1	6"x3/4"	TEE REDUCING 6" × 3/4" P300
8	1	3/4"	FLANGE WELD-NECK 3/4" P300 RAISED FACE
9	2	3/4"	GASKET 3/4" P300 COMPRESSED SHEET
10	1	3/4"	VALVE, BALL, FLOATING 3/4" P300
11	2	3/4"	STUD SET 4 × 0.5" × 4-1/4" WITH 2 NUTS, FOR 3/4" P300
12	1	3/4"	FLANGE BLIND 3/4" P300 RAISED FACE

REV	DATE	DESCRIPTION	BY
0	2026-11-01	ISSUED FOR CONSTRUCTION	-
1	2026-11-02	REVISED TO MATCH THE MODEL (FL-1)	-

NOTES:
1. ALL DIMENSIONS IN FEET AND INCHES UNLESS NOTED
2. BEVEL ENDS FOR BUTT WELD

TEST PRESS.	INSULATION	PAINT
-	NONE	-
PWHT	**NDE**	**FLUID**
-	-	P

COMPANY

SMARTWELD


TITLE

HYDROCARBON PROCESS

LINE NO.	PIPING CLASS	DESIGN PRESS.	DESIGN TEMP.
6"-P300-P-1011	H300	300 PSIG	-

DRAWING NO.	SHEET	REV
ISO-P-1011	1 OF 2	1

DATE	DRAWN	CHECKED	SCALE
2026-11-01	-	-	NTS

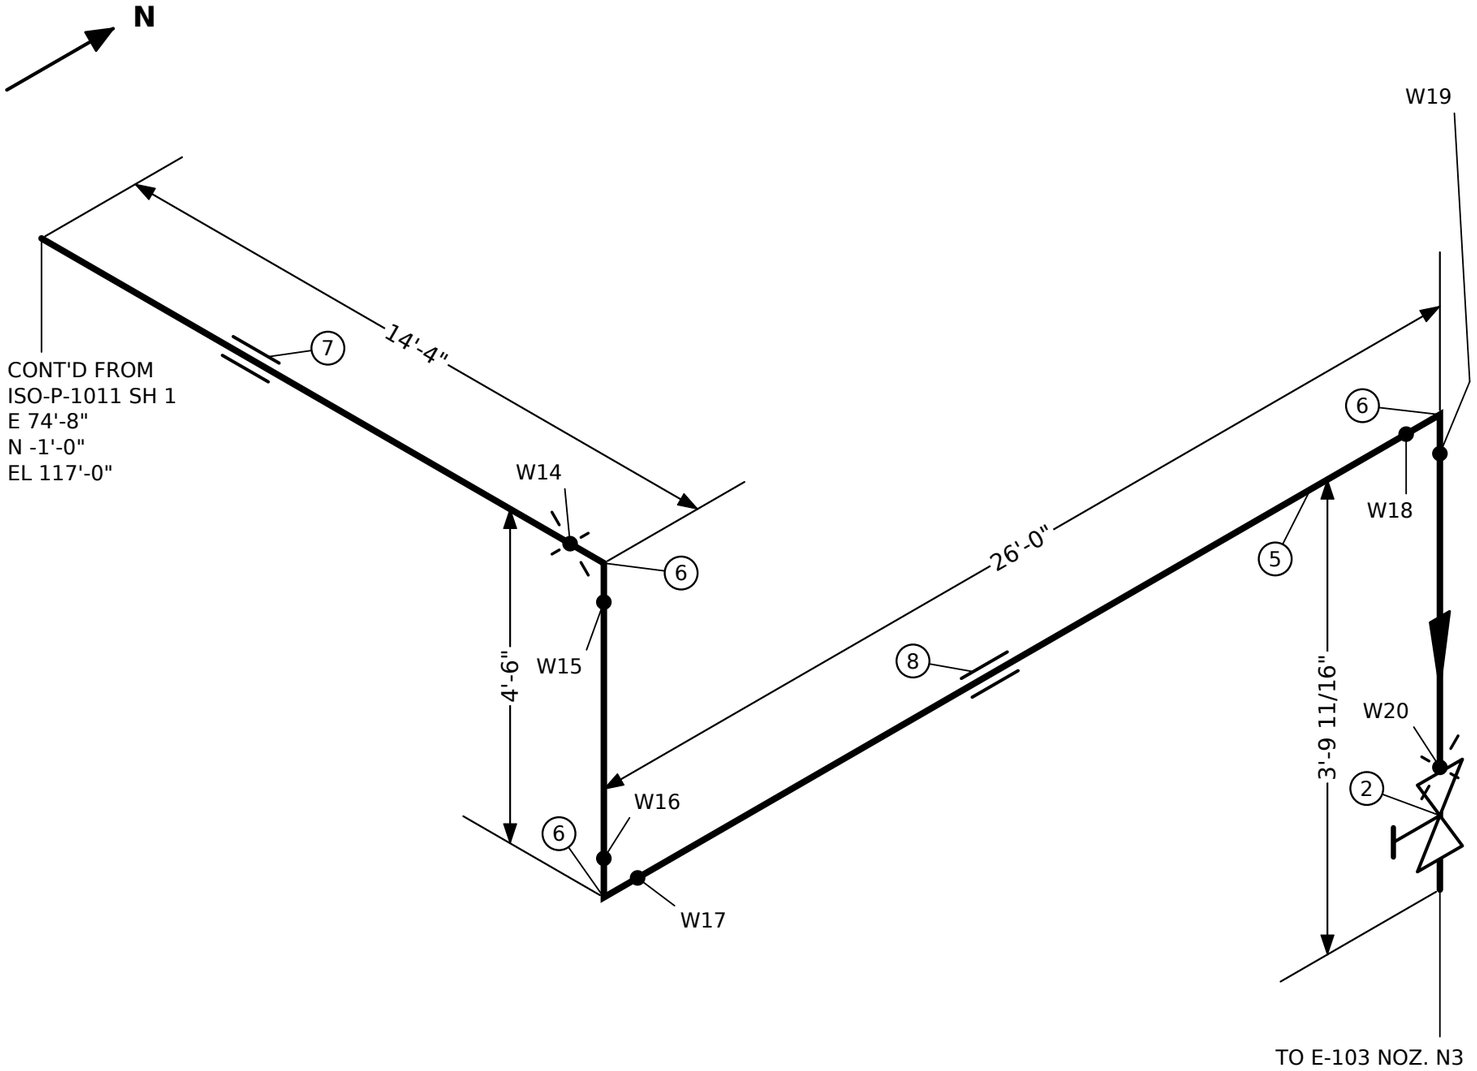

BILL OF MATERIALS

PT	QTY	NPS	DESCRIPTION
1	2	6"	GASKET 6" P300 COMPRESSED SHEET
2	1	6"	VALVE, GATE, WEDGE, OS&Y 6" P300
3	2	6"	STUD SET 8 × 0.625" × 4" WITH 2 NUTS, FOR 6" P300
4	1	6"	FLANGE WELD-NECK 6" P300 RAISED FACE
5	42'-1 1/2"	6"	PIPE 6" P300 BEVELLED ENDS
6	3	6"	ELBOW 90° R = 5/3 OD 6" P300
7	1	6"	ANCHOR FOR 6" LINE (ANCHOR-6)
8	1	6"	HANGER FOR 6" LINE (HANGER-6x238.0)

NOTES:

1. ALL DIMENSIONS IN FEET AND INCHES UNLESS NOTED
2. BEVEL ENDS FOR BUTT WELD

REV	DATE	DESCRIPTION	BY
0	2026-11-01	ISSUED FOR CONSTRUCTION	-
1	2026-11-02	REVISED TO MATCH THE MODEL (FL-1)	-

COMPANY

SMARTWELD

TITLE

HYDROCARBON PROCESS

TEST PRESS.	INSULATION	PAINT
-	NONE	-

PWHT	NDE	FLUID
-	-	P

LINE NO.	PIPING CLASS	DESIGN PRESS.	DESIGN TEMP.
6"-P300-P-1011	H300	300 PSIG	-

DRAWING NO.	SHEET	REV
ISO-P-1011	2 OF 2	1

DATE	DRAWN	CHECKED	SCALE
2026-11-01	-	-	NTS

Notices

DEMONSTRATION ONLY — NOT A QUALIFIED PROCEDURE; THE FACILITY OWNER'S QUALIFIED PROCEDURES AND APPLICABLE CODES GOVERN.

This document embeds a subset of the DejaVu Sans font (SW-LIC-3), renamed under its licence. DejaVu Sans (assets/fonts/DejaVuSans.ttf), from the DejaVu fonts 2.37 as packaged in the build environment.

Copyright (c) 2003 by Bitstream, Inc. All Rights Reserved. Bitstream Vera is a trademark of Bitstream, Inc.
DejaVu changes are in public domain.

Permission is hereby granted, free of charge, to any person obtaining a copy
of the fonts accompanying this license ("Fonts") and associated
documentation files (the "Font Software"), to reproduce and distribute the
Font Software, including without limitation the rights to use, copy, merge,
publish, distribute, and/or sell copies of the Font Software, and to permit
persons to whom the Font Software is furnished to do so, subject to the
following conditions:

The above copyright and trademark notices and this permission notice shall
be included in all copies of one or more of the Font Software typefaces.

The Font Software may be modified, altered, or added to, and in particular
the designs of glyphs or characters in the Fonts may be modified and
additional glyphs or characters may be added to the Fonts, only if the fonts
are renamed to names not containing either the words "Bitstream" or the word
"Vera".

This License becomes null and void to the extent applicable to Fonts or Font
Software that has been modified and is distributed under the "Bitstream
Vera" names.

The Font Software may be sold as part of a larger software package but no
copy of one or more of the Font Software typefaces may be sold by itself.

THE FONT SOFTWARE IS PROVIDED "AS IS", WITHOUT WARRANTY OF ANY KIND, EXPRESS
OR IMPLIED, INCLUDING BUT NOT LIMITED TO ANY WARRANTIES OF MERCHANTABILITY,
FITNESS FOR A PARTICULAR PURPOSE AND NONINFRINGEMENT OF COPYRIGHT, PATENT,
TRADEMARK, OR OTHER RIGHT. IN NO EVENT SHALL BITSTREAM OR THE GNOME
FOUNDATION BE LIABLE FOR ANY CLAIM, DAMAGES OR OTHER LIABILITY, INCLUDING
ANY GENERAL, SPECIAL, INDIRECT, INCIDENTAL, OR CONSEQUENTIAL DAMAGES,
WHETHER IN AN ACTION OF CONTRACT, TORT OR OTHERWISE, ARISING FROM, OUT OF
THE USE OR INABILITY TO USE THE FONT SOFTWARE OR FROM OTHER DEALINGS IN THE
FONT SOFTWARE.

Except as contained in this notice, the names of Gnome, the Gnome
Foundation, and Bitstream Inc., shall not be used in advertising or
otherwise to promote the sale, use or other dealings in this Font Software
without prior written authorization from the Gnome Foundation or Bitstream
Inc., respectively. For further information, contact: fonts at gnome dot
org.
