DEMONSTRATION ONLY — NOT A QUALIFIED PROCEDURE; THE FACILITY OWNER'S QUALIFIED PROCEDURES AND APPLICABLE CODES GOVERN.

WO-400-04 — Remake flanged joint 3"-P300-P-1015/B25 on 3"-P300-P-1015

Area	A400 Pumps	**Task**	GJ Flanged joint remake
Priority	2 (integrity)	**Issued by**	Facility owner (demonstration)
Primary asset	P-103A — P-103A centrifugal pump — E 174'-0" N -18'-6" EL 100'-9"		
Equipment	P-103A	**Lines**	3"-P300-P-1015
Isometrics	ISO-P-1015 (owner's drawings, attached)		
Permits	General work permit		

Reason

Weeping joint at the control valve station.

Scope of work

1. Isolate per the isolation list, drain and vent 3"-P300-P-1015.
2. Break the joint at E 68'-6" N 13'-9-11/16" EL 125'-0" between VALVE, GATE, WEDGE, OS&Y 3" P300 and FLANGE WELD-NECK 3" P300 RAISED FACE.
3. Inspect both flange faces (SW-NDE-5).
4. Fit a new gasket and new studs; tighten to the stated preload in three passes, cross pattern (SW-WO-5).
5. Remove blinds; leak test on start-up (SW-TEST-2).

Affected items: 3"-P300-P-1015/B25, 3"-P300-P-1015/B26, 3"-P300-P-1015/B24

Rules: SW-ITP-1, SW-ITP-2, SW-ITP-3, SW-NDE-5, SW-TEST-2, SW-WO-1, SW-WO-2, SW-WO-3, SW-WO-5, SW-WO-7

Owner's isometric drawings (SW-IMP-6)

Drawing	Line drawn	Work line	Sheets	Match to the plant model
ISO-P-1015	3"-P300-P-1015	3"-P300-P-1015	6	agrees with the model

ISO-P-1015 (PDF): ../isometrics-imported/ISO-P-1015.pdf — the sheets that hold the work follow the ITP.

Assets in the plant model (SW-WO-7)

Tag	Kind	Description	Line	Location
P-103A	equipment	P-103A centrifugal pump		E 174'-0" N -18'-6" EL 100'-9"
3"-P300-P-1015/B25	item	GASKET 3" P300 COMPRESSED SHEET	3"-P300-P-1015	E 68'-6" N 13'-9-11/16" EL 125'-0"
3"-P300-P-1015/B26	item	VALVE, GATE, WEDGE, OS&Y 3" P300	3"-P300-P-1015	E 68'-6" N 13'-2-13/16" EL 125'-0"
3"-P300-P-1015/B24	item	FLANGE WELD-NECK 3" P300 RAISED FACE	3"-P300-P-1015	E 68'-6" N 14'-5/16" EL 125'-0"
3"-P300-P-1015/A10	item	VALVE, GATE, WEDGE, OS&Y 3" P300	3"-P300-P-1015	E 174'-0" N -16'-6" EL 106'-6-9/16"
3"-P300-P-1015/A13	item	FLANGE WELD-NECK 3" P300 RAISED FACE	3"-P300-P-1015	E 174'-0" N -16'-6" EL 107'-4"
3"-P300-P-1015/B10	item	VALVE, GATE, WEDGE, OS&Y 3" P300	3"-P300-P-1015	E 68'-6" N 18'-3-11/16" EL 125'-0"
3"-P300-P-1015/B13	item	FLANGE WELD-NECK 3" P300 RAISED FACE	3"-P300-P-1015	E 68'-6" N 17'-6-3/16" EL 125'-0"

Isolation list (SW-WO-3)

#	Kind	Tag	Line	Action	Location	Fitted ✓	Removed ✓
1	valve	3"-P300-P-1015/A10	3"-P300-P-1015	Close and lock VALVE, GATE, WEDGE, OS&Y 3" P300 (3"-P300-P-1015/A10)	E 174'-0" N -16'-6" EL 106'-6-9/16"		
2	blind	3"-P300-P-1015/A13	3"-P300-P-1015	Fit a line blind between 3"-P300-P-1015/A10 and FLANGE WELD-NECK 3" P300 RAISED FACE (3"-P300-P-1015/A13), work side	E 174'-0" N -16'-6" EL 107'-1-7/16"		
3	valve	3"-P300-P-1015/B10	3"-P300-P-1015	Close and lock VALVE, GATE, WEDGE, OS&Y 3" P300 (3"-P300-P-1015/B10)	E 68'-6" N 18'-3-11/16" EL 125'-0"		
4	blind	3"-P300-P-1015/B13	3"-P300-P-1015	Fit a line blind between 3"-P300-P-1015/B10 and FLANGE WELD-NECK 3" P300 RAISED FACE (3"-P300-P-1015/B13), work side	E 68'-6" N 17'-8-3/4" EL 125'-0"		

Parts

Description	Qty	Replaces
GASKET 3" P300 COMPRESSED SHEET	1	3"-P300-P-1015/B25
STUD SET 4 × 0.875" × 5-3/4" WITH 2 NUTS, FOR 3" P300	1	3"-P300-P-1015/B27

Inspections

Id	Inspection	Criteria	Basis
WO-400-04-I1	Flange faces before the new gasket goes in	No radial scratch across the sealing face (SW-NDE-5)	SW-NDE-5

Bolt-up (SW-WO-5)

Joint	Studs	Preload per stud (lbf)	Passes	Done ✓
3"-P300-P-1015/B25	4 × 0.875" studs (3"-P300-P-1015/B27)	27,059	3	

Test — Service leak test

Description	The remade joint checked at operating pressure on start-up
Basis	SW-TEST-2

Inspection and test plan (SW-ITP-1..3)


H hold · W witness · R review · S surveillance. Status: accepted / rejected / not applicable.

#	Activity	Reference	Acceptance	Record	Contr.	Owner	3rd party	Status	Signed (contr. / owner / 3rd)	Date	Remark
1	Work permit issued; isolation list (valves locked, blinds fitted) verified at zero pressure and drained	SW-WO-3, isolation list	Every isolation in place and tagged; zero pressure at the vent	Signed isolation certificate	H	H	—				
2	Joint broken; both flange faces inspected	SW-NDE-5	No radial scratch across the sealing face	Flange face inspection record	W	W	—				
3	New gasket fitted; studs tightened to preload in three passes	SW-WO-5	Preload per stud as stated	Bolt-up record	W	W	—				
4	Service leak test on start-up	SW-TEST-2	No leak	Leak test record	W	W	—				
5	Blinds removed, isolations returned to normal line-up per the isolation list	SW-WO-3	Every blind removed and accounted for	Isolation certificate closed	H	H	—				
6	Records complete; work order handed back to operations	SW-ITP-3	All ITP activities accepted or not applicable	Signed ITP and completion record	H	H	R				

Where the work is on the owner's drawings (SW-IMP-8)

Each affected item, replaced weld and isolation point, with the drawing and sheet that hold it and the weld label printed there. The sheets follow, copied unchanged.

Tag	Role	Drawing	Sheet	Weld label
3"-P300-P-1015/B25	affected	ISO-P-1015	6	
3"-P300-P-1015/B26	affected	ISO-P-1015	6	
3"-P300-P-1015/B24	affected	ISO-P-1015	6	
3"-P300-P-1015/A10	isolation: valve	ISO-P-1015	1	
3"-P300-P-1015/A13	isolation: blind	ISO-P-1015	1	
3"-P300-P-1015/B10	isolation: valve	ISO-P-1015	6	
3"-P300-P-1015/B13	isolation: blind	ISO-P-1015	6	

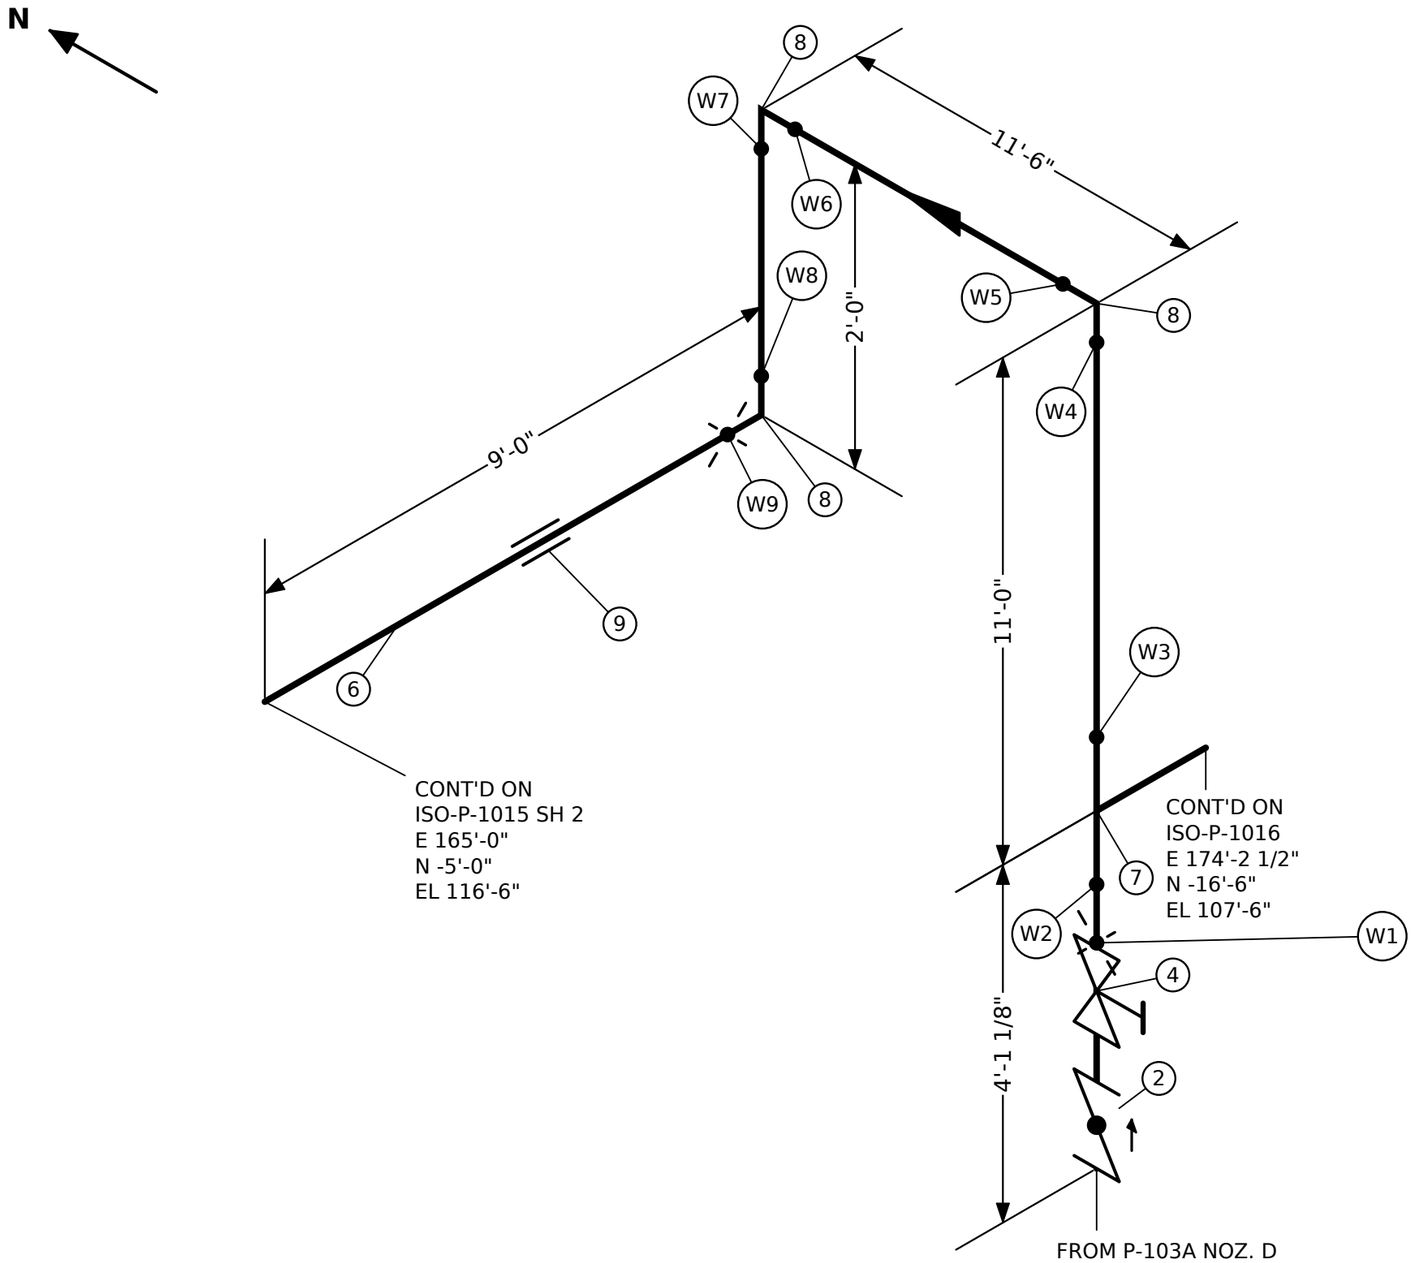

BILL OF MATERIALS

PT	QTY	NPS	DESCRIPTION
1	3	3"	GASKET 3" P300 COMPRESSED SHEET
2	1	3"	VALVE, SWING CHECK 3" P300
3	3	3"	STUD SET 4 × 0.875" × 5-3/4" WITH 2 NUTS, FOR 3" P300
4	1	3"	VALVE, GATE, WEDGE, OS&Y 3" P300
5	1	3"	FLANGE WELD-NECK 3" P300 RAISED FACE
6	31'-10 13/16"	3"	PIPE 3" P300 BEVELLED ENDS
7	1	3"	TEE EQUAL 3" P300
8	3	3"	ELBOW 90° R = 5/3 OD 3" P300
9	1	3"	SHOE FOR 3" LINE (SHOE-3)

REV	DATE	DESCRIPTION	BY
0	2026-11-01	ISSUED FOR CONSTRUCTION	-
1	2026-11-02	REVISED TO MATCH THE MODEL (FL-1)	-

COMPANY

SMARTWELD

TITLE

HYDROCARBON PROCESS

NOTES:


1. ALL DIMENSIONS IN FEET AND INCHES UNLESS NOTED
2. BEVEL ENDS FOR BUTT WELD
3. FLANGE BOLT HOLES STRADDLE CENTRELINES

TEST PRESS.	INSULATION	PAINT
-	NONE	-
PWHT	NDE	FLUID
-	-	P

LINE NO.	PIPING CLASS	DESIGN PRESS.	DESIGN TEMP.
3"-P300-P-1015	H300	300 PSIG	-

DRAWING NO.	SHEET	REV
ISO-P-1015	1 OF 6	1

DATE	DRAWN	CHECKED	SCALE
2026-11-01	-	-	NTS

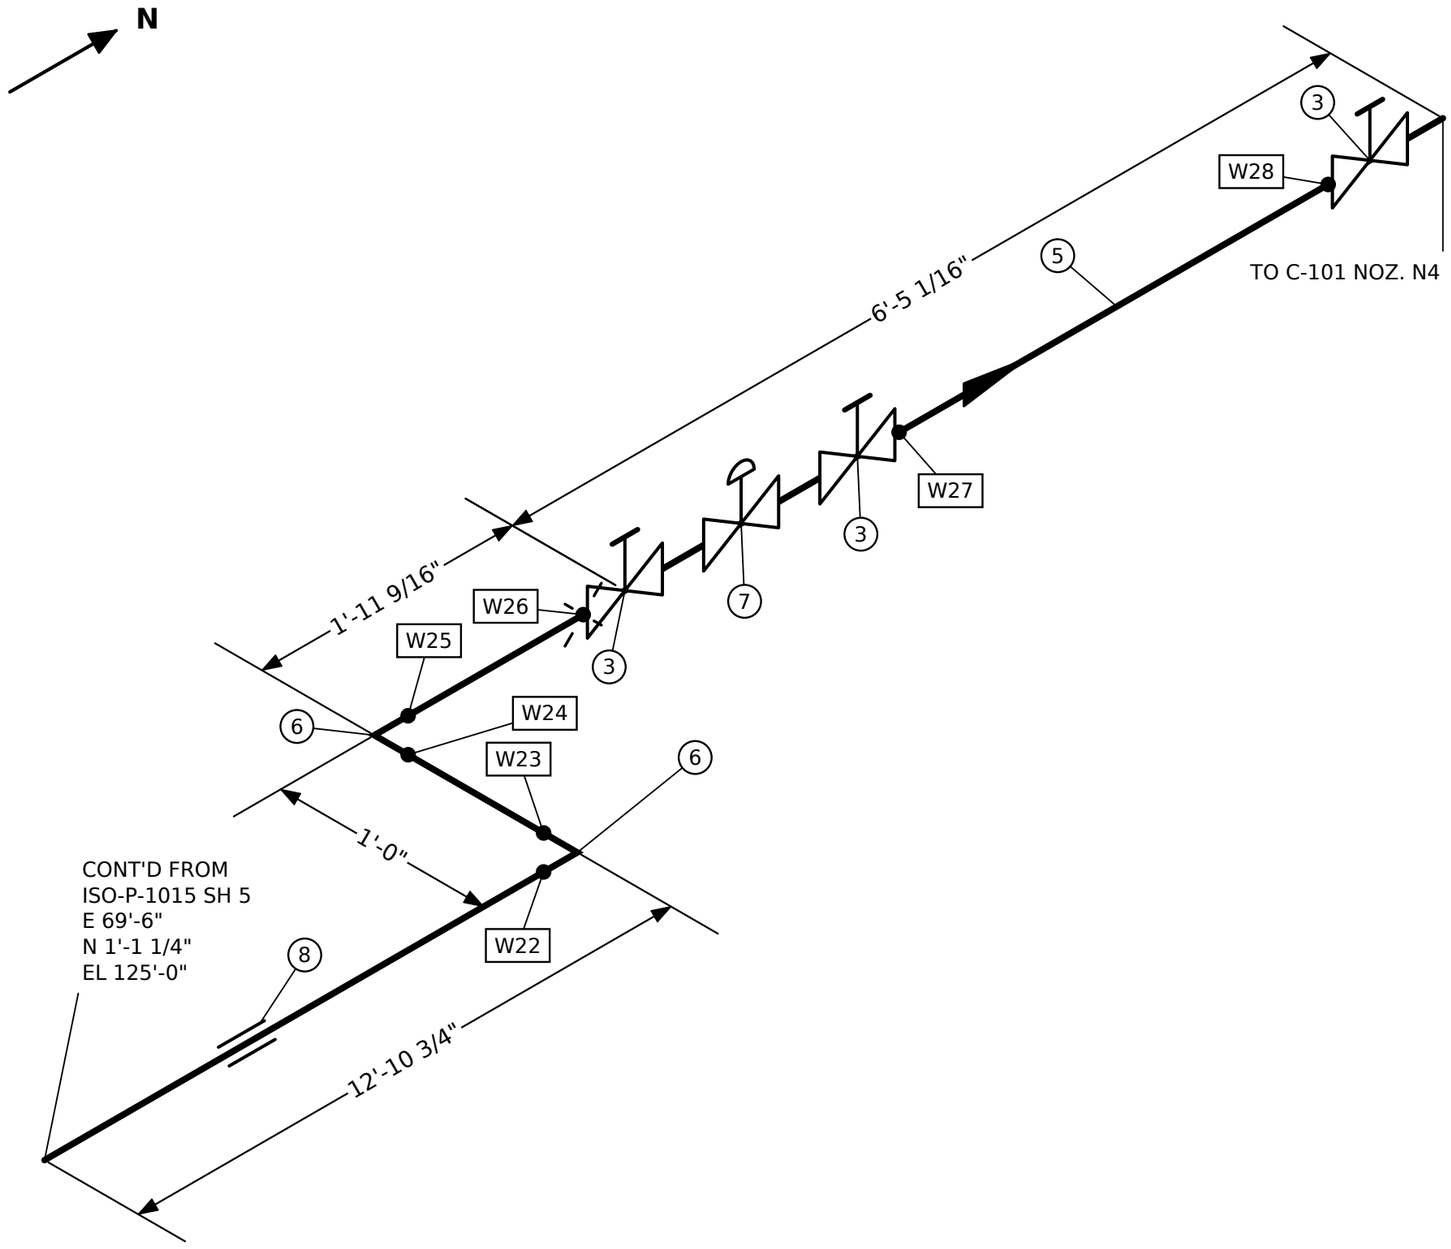

BILL OF MATERIALS

PT	QTY	NPS	DESCRIPTION
1	6	3"	GASKET 3" P300 COMPRESSED SHEET
2	6	3"	STUD SET 4 × 0.875" × 5-3/4" WITH 2 NUTS, FOR 3" P300
3	3	3"	VALVE, GATE, WEDGE, OS&Y 3" P300
4	3	3"	FLANGE WELD-NECK 3" P300 RAISED FACE
5	14'-8 5/16"	3"	PIPE 3" P300 BEVELLED ENDS
6	2	3"	ELBOW 90° R = 5/3 OD 3" P300
7	1	3"	VALVE, CONTROL, GLOBE WITH DIAPHRAGM ACTUATOR 3" P300
8	1	3"	HANGER FOR 3" LINE (HANGER-3x93.0)

REV	DATE	DESCRIPTION	BY
0	2026-11-01	ISSUED FOR CONSTRUCTION	-
1	2026-11-02	REVISED TO MATCH THE MODEL (FL-1)	-

COMPANY

SMARTWELD

TITLE

HYDROCARBON PROCESS

NOTES:

1. ALL DIMENSIONS IN FEET AND INCHES UNLESS NOTED
2. BEVEL ENDS FOR BUTT WELD
3. FLANGE BOLT HOLES STRADDLE CENTRELINES
4. PAINT PER PROJECT SPECIFICATION

TEST PRESS.	INSULATION	PAINT
-	NONE	-
PWHT	NDE	FLUID
-	-	P

LINE NO.	PIPING CLASS	DESIGN PRESS.	DESIGN TEMP.
3"-P300-P-1015	H300	300 PSIG	-

DRAWING NO.	SHEET	REV
ISO-P-1015	6 OF 6	1

DATE	DRAWN	CHECKED	SCALE
2026-11-01	-	-	NTS

Notices

DEMONSTRATION ONLY — NOT A QUALIFIED PROCEDURE; THE FACILITY OWNER'S QUALIFIED PROCEDURES AND APPLICABLE CODES GOVERN.

This document embeds a subset of the DejaVu Sans font (SW-LIC-3), renamed under its licence. DejaVu Sans (assets/fonts/DejaVuSans.ttf), from the DejaVu fonts 2.37 as packaged in the build environment.

Copyright (c) 2003 by Bitstream, Inc. All Rights Reserved. Bitstream Vera is a trademark of Bitstream, Inc.
DejaVu changes are in public domain.

Permission is hereby granted, free of charge, to any person obtaining a copy
of the fonts accompanying this license ("Fonts") and associated
documentation files (the "Font Software"), to reproduce and distribute the
Font Software, including without limitation the rights to use, copy, merge,
publish, distribute, and/or sell copies of the Font Software, and to permit
persons to whom the Font Software is furnished to do so, subject to the
following conditions:

The above copyright and trademark notices and this permission notice shall
be included in all copies of one or more of the Font Software typefaces.

The Font Software may be modified, altered, or added to, and in particular
the designs of glyphs or characters in the Fonts may be modified and
additional glyphs or characters may be added to the Fonts, only if the fonts
are renamed to names not containing either the words "Bitstream" or the word
"Vera".

This License becomes null and void to the extent applicable to Fonts or Font
Software that has been modified and is distributed under the "Bitstream
Vera" names.

The Font Software may be sold as part of a larger software package but no
copy of one or more of the Font Software typefaces may be sold by itself.

THE FONT SOFTWARE IS PROVIDED "AS IS", WITHOUT WARRANTY OF ANY KIND, EXPRESS
OR IMPLIED, INCLUDING BUT NOT LIMITED TO ANY WARRANTIES OF MERCHANTABILITY,
FITNESS FOR A PARTICULAR PURPOSE AND NONINFRINGEMENT OF COPYRIGHT, PATENT,
TRADEMARK, OR OTHER RIGHT. IN NO EVENT SHALL BITSTREAM OR THE GNOME
FOUNDATION BE LIABLE FOR ANY CLAIM, DAMAGES OR OTHER LIABILITY, INCLUDING
ANY GENERAL, SPECIAL, INDIRECT, INCIDENTAL, OR CONSEQUENTIAL DAMAGES,
WHETHER IN AN ACTION OF CONTRACT, TORT OR OTHERWISE, ARISING FROM, OUT OF
THE USE OR INABILITY TO USE THE FONT SOFTWARE OR FROM OTHER DEALINGS IN THE
FONT SOFTWARE.

Except as contained in this notice, the names of Gnome, the Gnome
Foundation, and Bitstream Inc., shall not be used in advertising or
otherwise to promote the sale, use or other dealings in this Font Software
without prior written authorization from the Gnome Foundation or Bitstream
Inc., respectively. For further information, contact: fonts at gnome dot
org.
